

## 21st Century School Buildings Program

Commodore John Rodgers Elementary/Middle School COMMUNITY MEETING – CONSTRUCTION UPDATE September 18, 2025













## Introductions and Agenda


Presenters	Agenda
Ivy McNeill Senior Program Manager – Community Engagement	Procurement Update
21st Century School Buildings Program	Work Progress
Cyndi Smith	Schedule
Executive Director, Facilities Planning, Design and Construction – Baltimore City Public Schools	Site Plan
	Floor Plans
Charlie Ravenna Project Director	Renderings
Maryland Stadium Authority	• Q&A
Construction Manager	
CAM Construction	

### **Procurement Updates**






- The State of Maryland Board of Public Works (BPW) approvals:
  - Pre-Construction Services
     Contract to CAM Construction,
     August 7, 2024.
  - CAM Construction GMP-1, October 2, 2024.
  - CAM Construction GMP
     December 4, 2024.
- The only remaining procurement is Furnishing Furniture & Equipment (FFE) which is being procured by City Schools and will not begin the procurement process until the Late Summer / Fall 2025

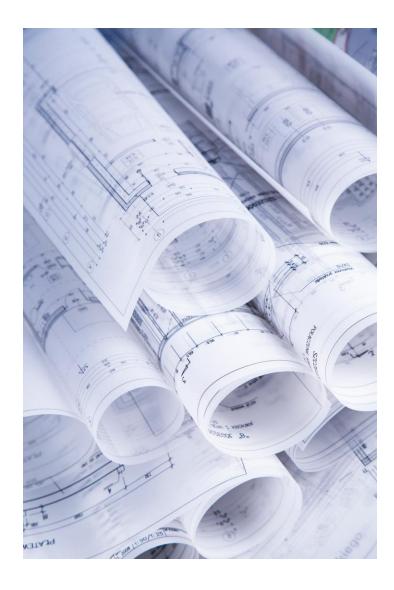



- CMU foundations & concrete floor slab-on-grade started May 2025 and finished Aug 2025.
- CMU bearing walls above grade are underway and will continue through December 2025. Bearing walls then interior walls.
- Structural steel started in Aug 2025 and will continue through December 2025. Areas A-B to C
- Elevated concrete floor slabs will follow structural steel areas A-B to C. 2<sup>nd</sup> floors then 3<sup>rd</sup> floors.
- Building envelope walls will follow the elevated concrete slabs and will continue through Winter 2025/2026.
- Street utilities are underway and will continue through Spring 2026. From the street onto site then to the building following the building envelope.


## Progress Photos - 12/9/2024

## Construction

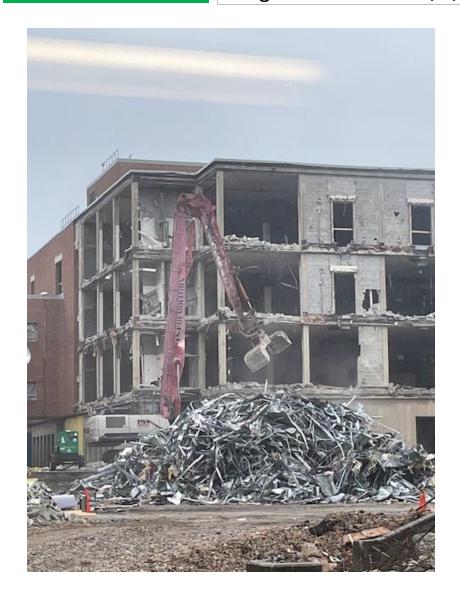


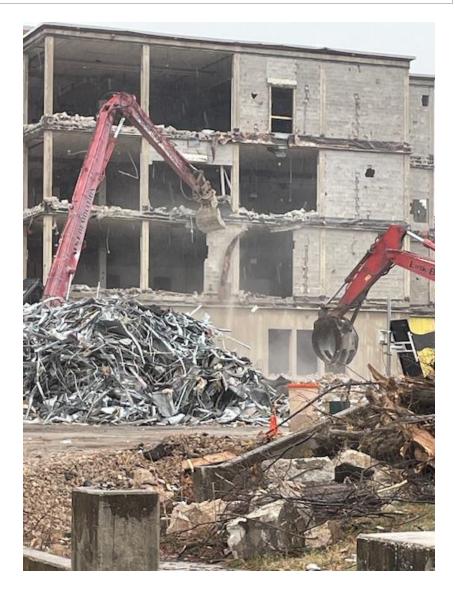

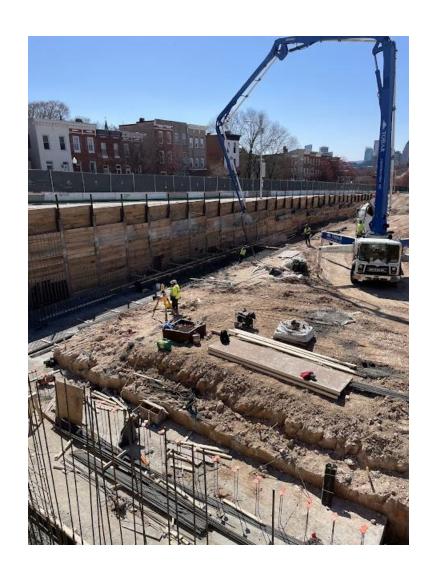

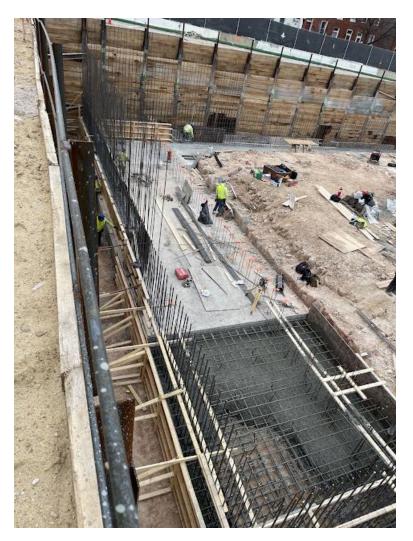


## Progress Photos - 5/1/2025

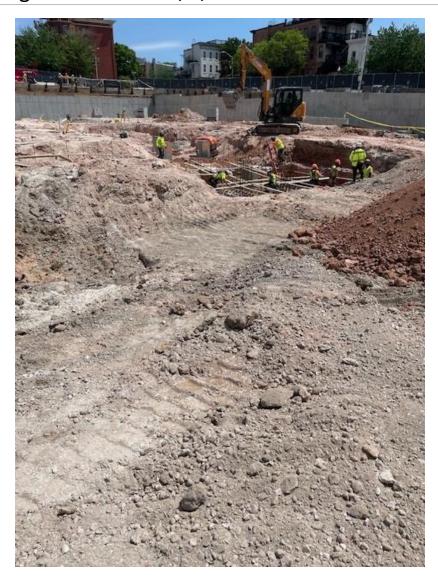


Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025


## Progress Photos - 5/7/2025

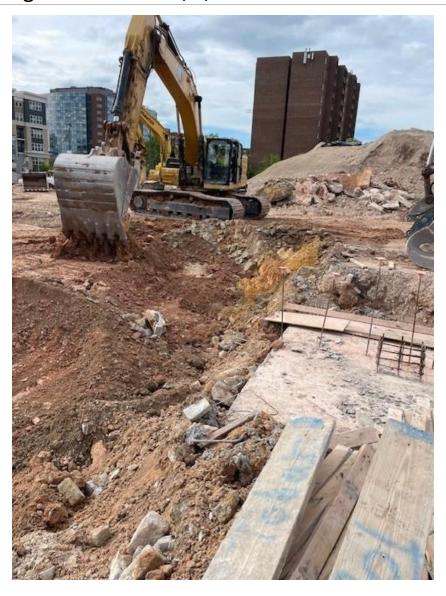

Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

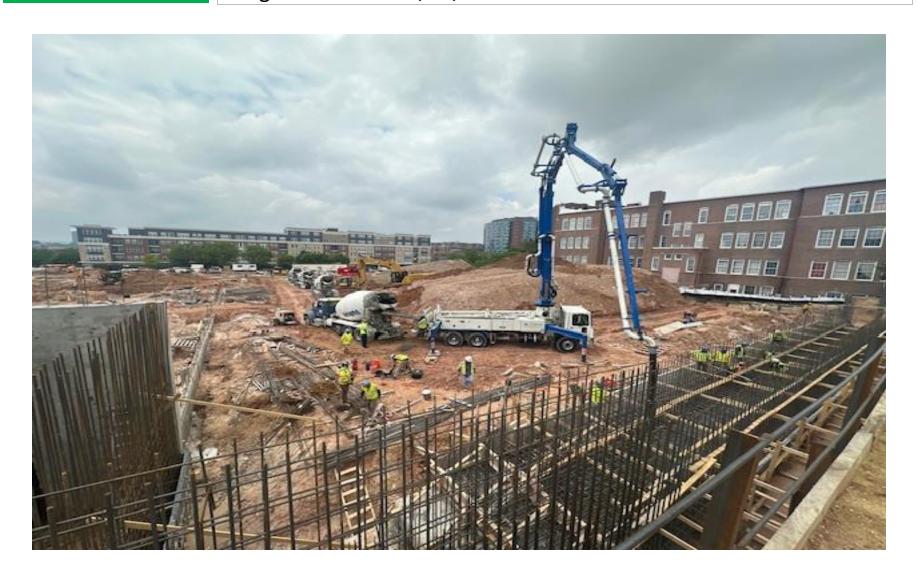

## Progress Photos - 5/16/2025

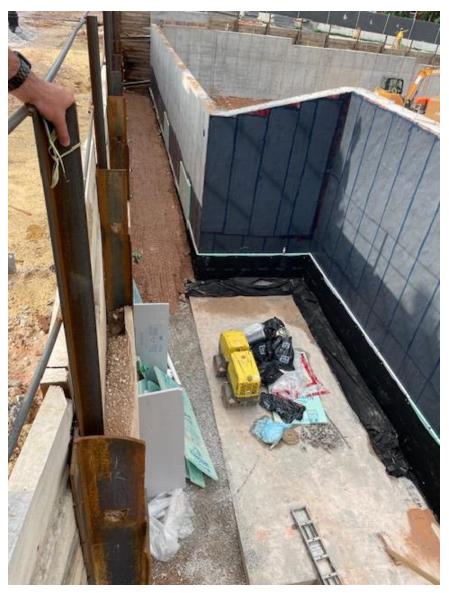


Commodore John Rodgers E/MS Community Meeting | Construction Update September18, 2025

## Progress Photos - 5/26/2025



Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

## Progress Photos - 5/29/2025

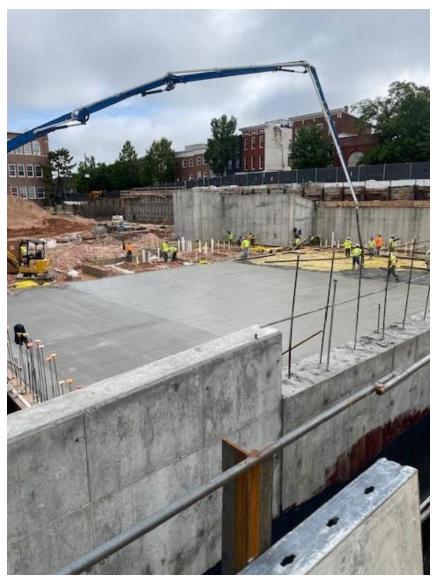

Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025




Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

## Progress Photos - 6/13/2025





Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025



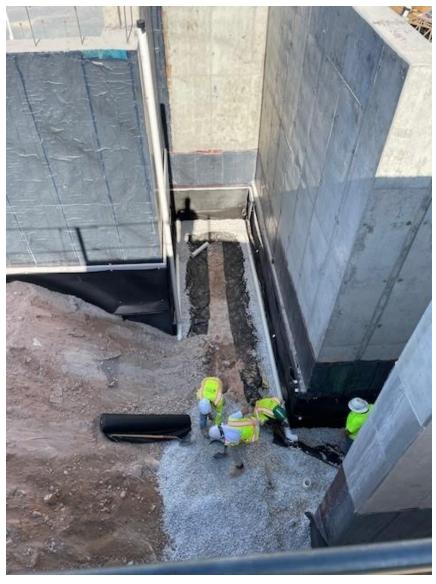



Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

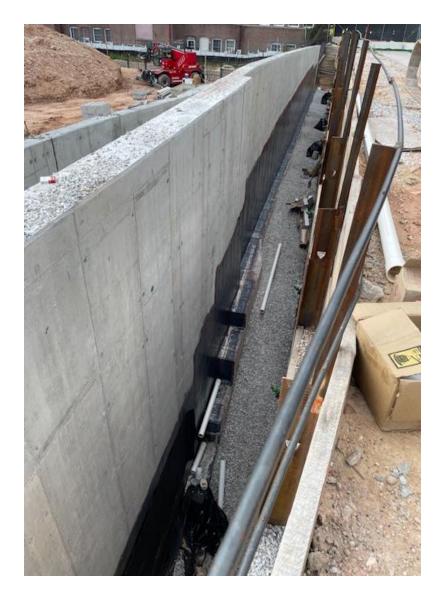

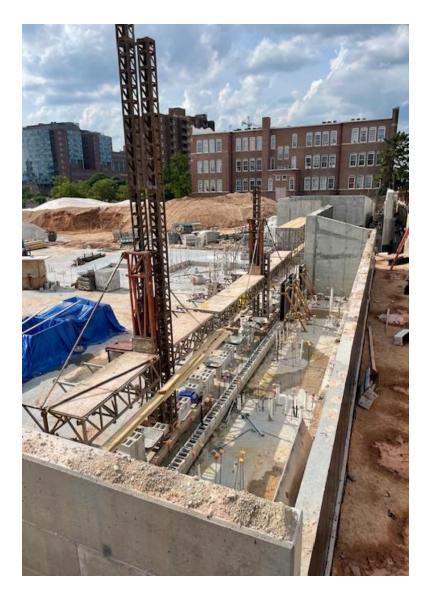

Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

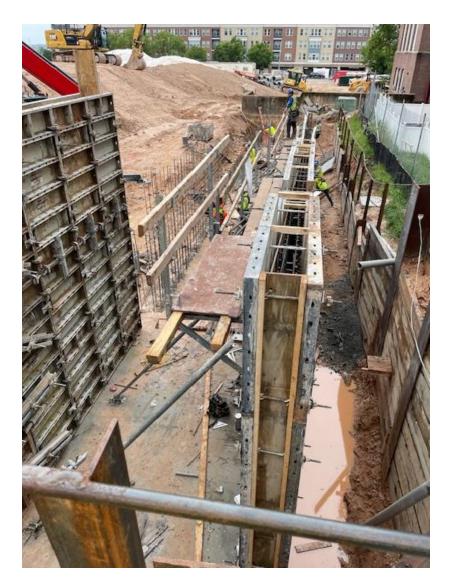

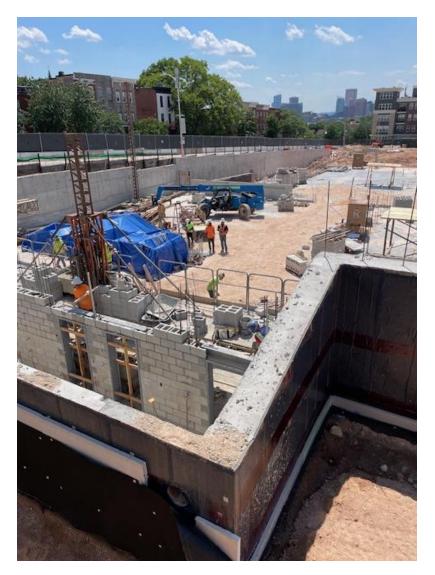

Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

## Progress Photos - 7/16/2025



Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025





Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

## Progress Photos - 8/5/2025




Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

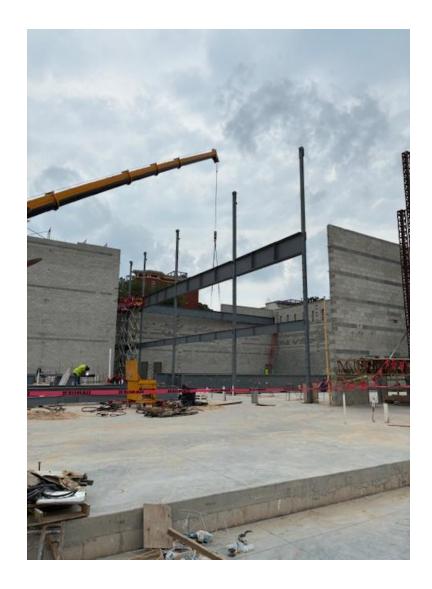

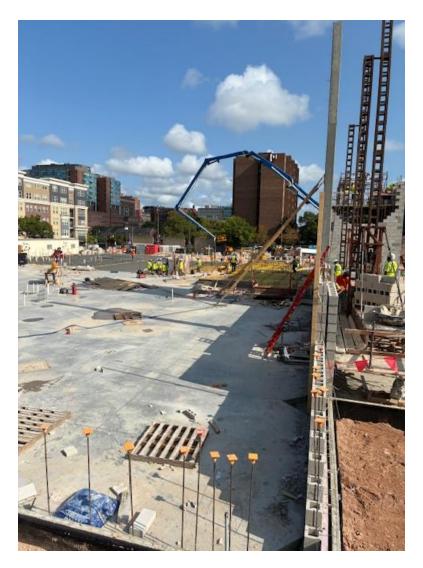




Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

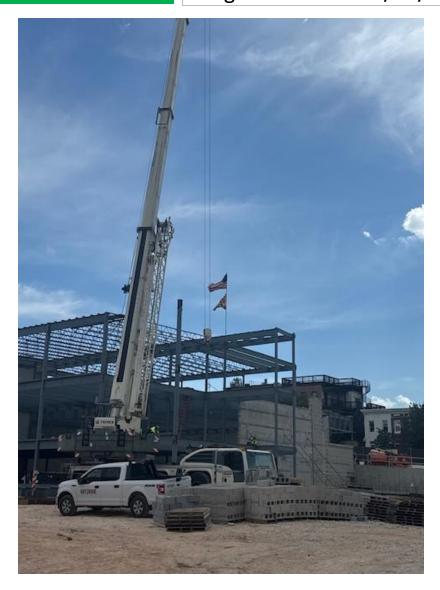







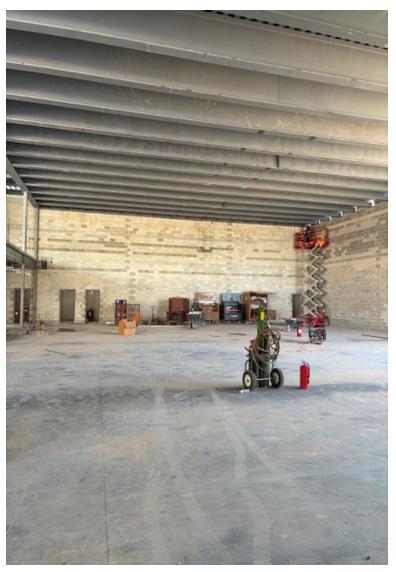


Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

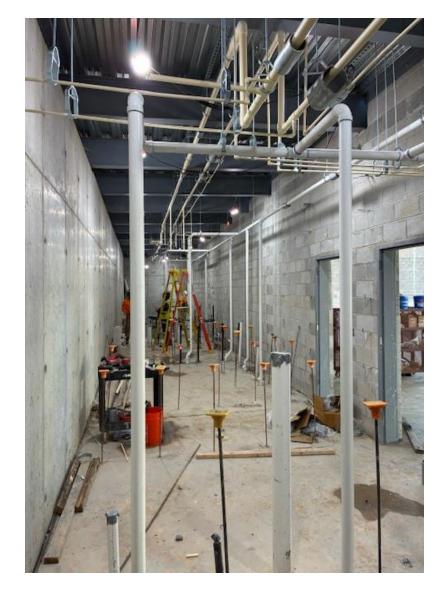

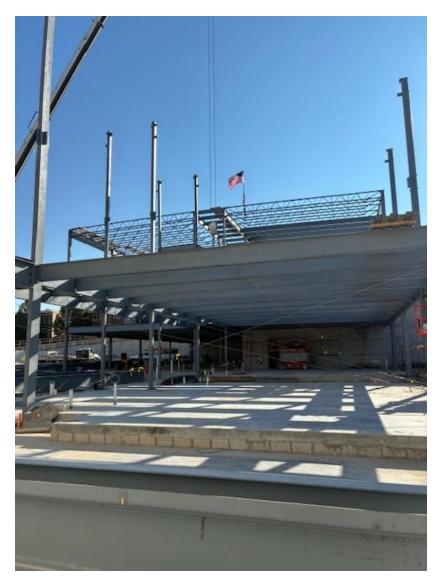


Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

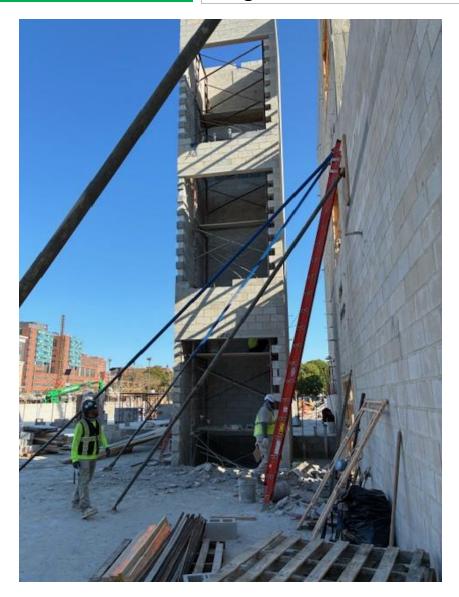




Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

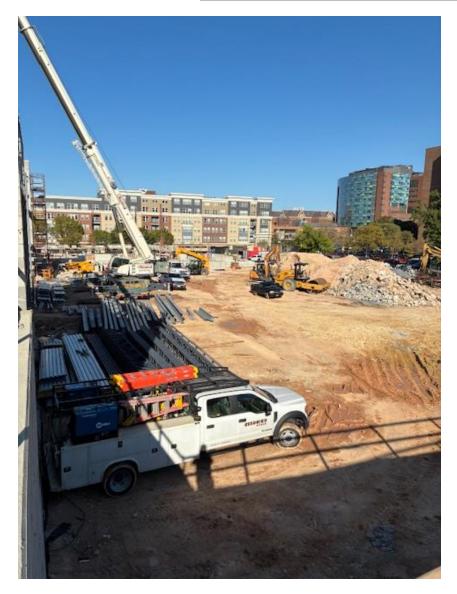





Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

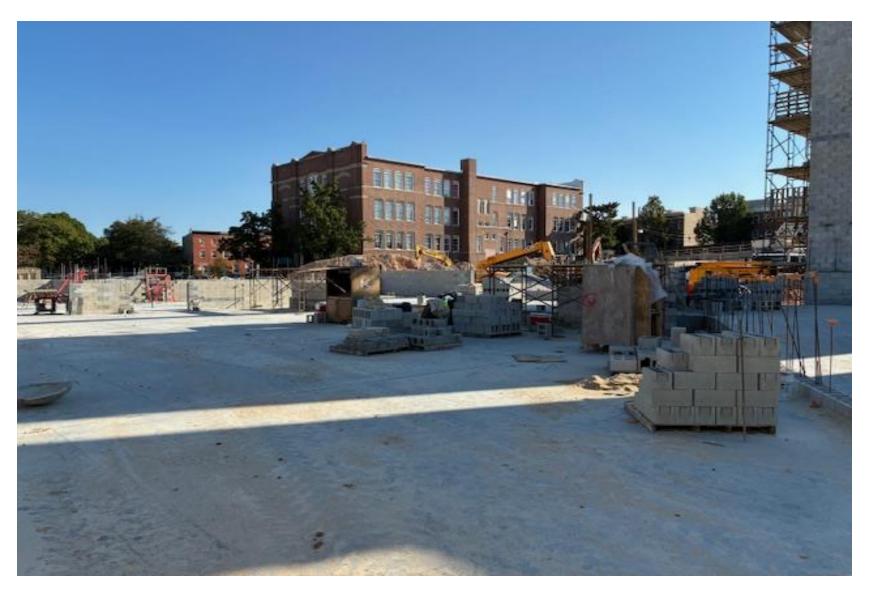

Commodore John Rodgers E/MS Community Meeting | Construction Update September18, 2025

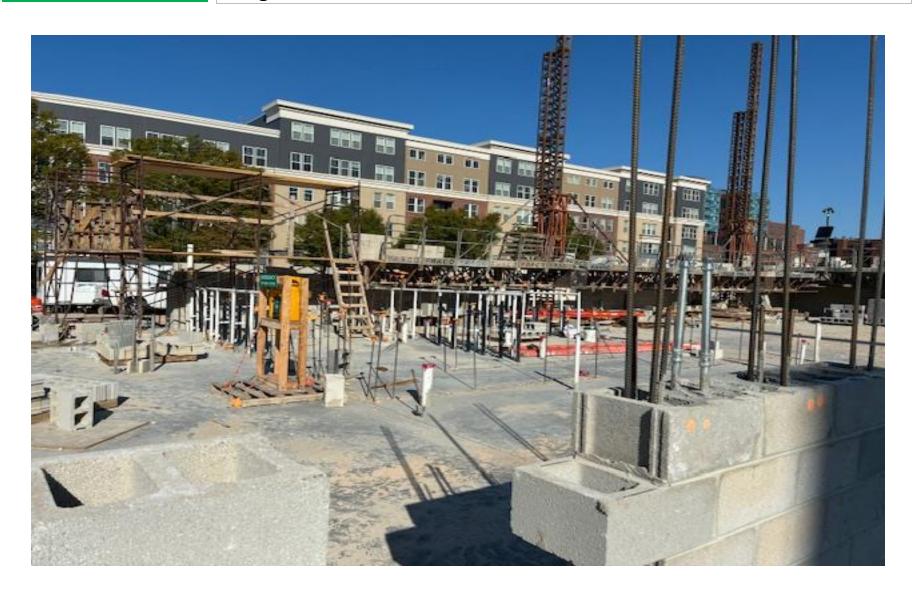

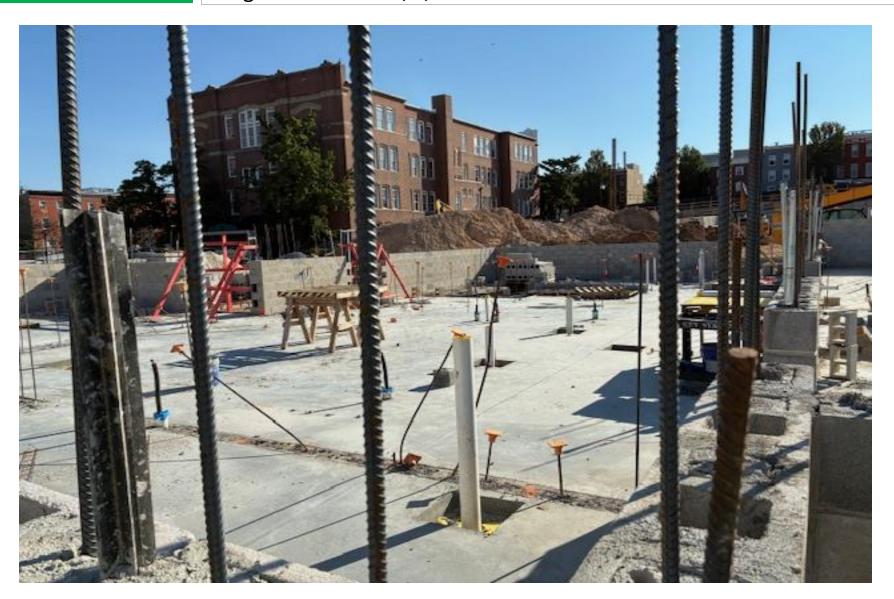

Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025

Abatement then Demolition

Start:

Oct 7, 2024

Parking Lane & Sidewalk

Closures Adjacent to the

**Building Start:** 

Oct 15, 2024

Building Construction Start: Spring 2025

Substantial Completion: November 30, 2026\*

Occupancy: December 2026\*

<sup>\*</sup> Dates listed are based on a projected schedule and are subject to change.

### Design

### Overall Site Plan Design



#### **Site Features**

- Main entrance on N. Washington Ave. –
  provides bus and vehicular access at main
  entrance location
- Secure play area from northeast neighborhood at N. Chester Street

### **Safety & Security**

- Defined main entrance at bus and parent drop-off
- Three separate and secured play areas
- Dedicated staff, visitor, and community parking totaling 34 spaces

### **Site Opportunities**

 Re-oriented building and site to optimize use of available space


## Pedestrian Circulation & Community Connectivity

 Main entrance and parking provide access to all community support spaces.



### Design

### First Floor Plan

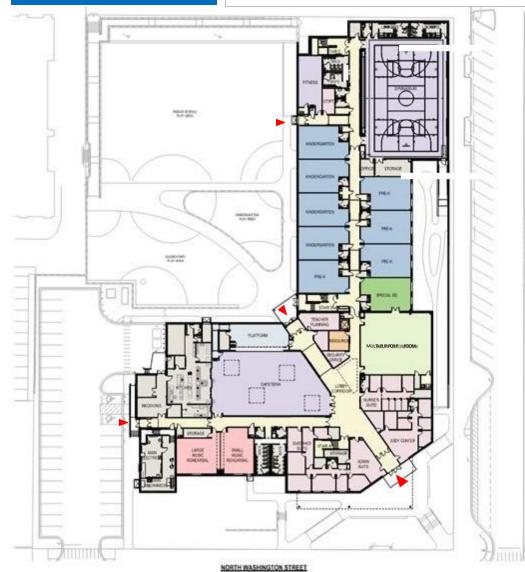

- Pre-K-Kindergarten grades
- Special education classroom
- Music classrooms
- Multi-Purpose Room
- Gym/Fitness and support spaces
- Cafetorium/Platform
- Teacher Planning
- Administration
- Guidance
- Health suite
- Family resource room
- Judy Center




First Floor GSF: 53,43 SF Overall SF: 118,073 SF

### Second Floor Plan



- Grades 1-4
- Special education classroom
- Speech
- Art classrooms
- Media center/Video room
- Flexible Classroom opportunity






Second Floor GSF: 31,858 SF Overall SF: 118,073 SF

### Third Floor Plan



- Grades 5-8
- Special education classrooms
- Science classrooms
- Technology lab
- Resource rooms
- Flexible Teacher Planning





Third Floor GSF: 32,802 SF Overall SF: 118,073 SF Design

## Rendering – Main Entrance from North Washington Street




Design


## Rendering – Entrance from North Chester Street



## Rendering – Media Center

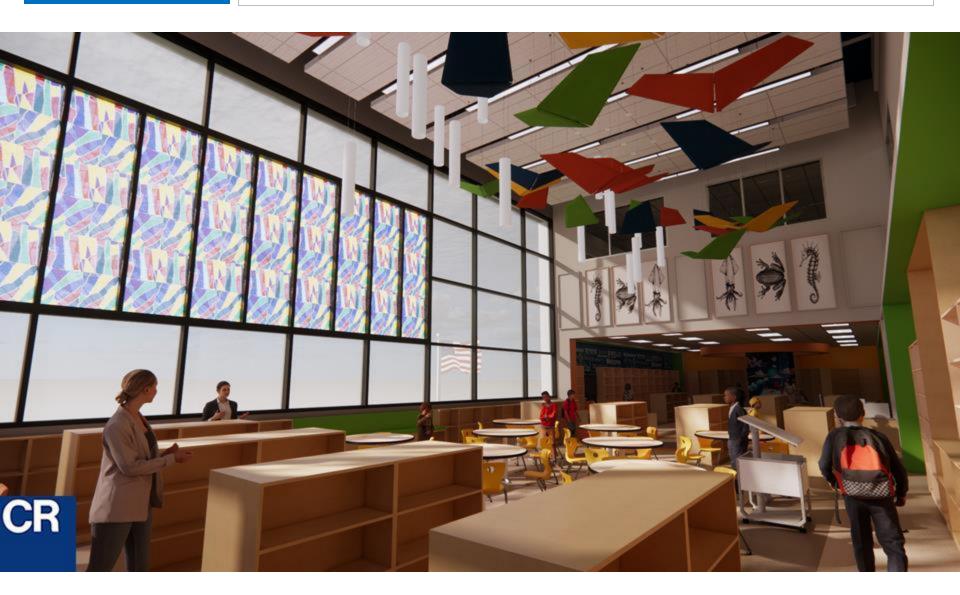

## Rendering – Gymnasium

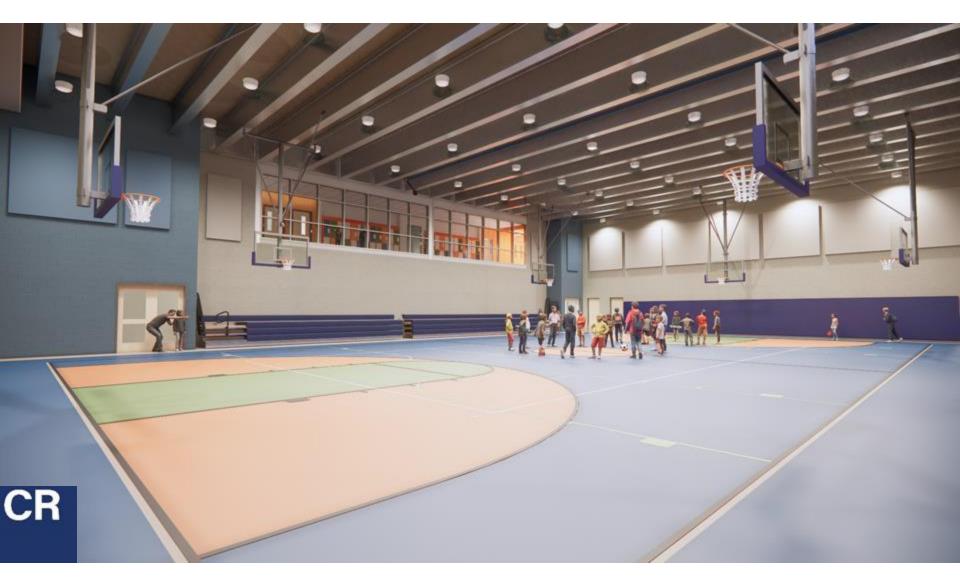

## Rendering – Cafeteria



## Baltimore21stCenturySchools.org

AA @ :altimore21stcenturyschools.org &

# FaceBook.com/ 21stCenturySchoolBuildingsProgram











## **Questions?**

## **Program Contacts**

Sr. Community & Public Relations Coordinator
Ivy McNeill

idmcneill01@bcps.k12.md.us

Director Community
Engagement & Strategic Partnerships
TaMikka Sykes
TCSykes@bcps.k12.md.us

## **Program Information**

21st Century School Buildings Program Office (443) 642-4600








#### Thank You.

This presentation was brought to you by the Baltimore City Schools Office of New Initiatives



Baltimore MD 21202 (443) 642-4600

www.baltimore21stcenturyschools.org











Commodore John Rodgers E/MS Community Meeting | Construction Update September 18, 2025
