

21st Century School Buildings Program

Cross Country Elementary/Middle School Replacement - Community Meeting #8


Construction Update Meeting

November 15, 2022

Introductions and Agenda

Presenters	Agenda
Renee Stainrod Manager, Community & Public Relations 21st Century School Buildings Program	 Introduction
Ivy McNeill Sr. Program Coordinator, Community & Engagement	Construction Schedule
21st Century School Buildings Program Miriam Carrion Spanish Translator Hispanic Advocate	Construction Overview
	• Parking
Michael Mc Bride Design Director 21st Century School Buildings Program	Schedule Target Dates
Catherine Acker Project Manager	Community Meeting Information
Maryland Stadium Authority	 Questions
Priya lyer Project Architect Colimore Architects, an ATI Company	
Robert Stone Sr. Project Manager Turner Construction Company	


Hours of Operation: Typical Day: 7am – 4pm Late Day: 7am – 7pm

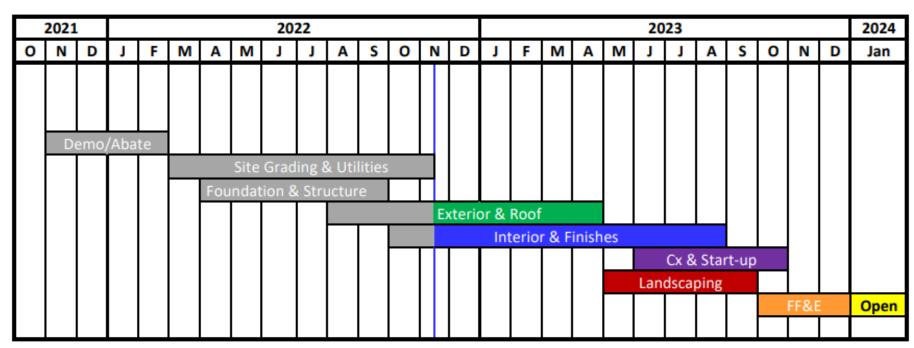



School Opening January 2024

Exterior Framing

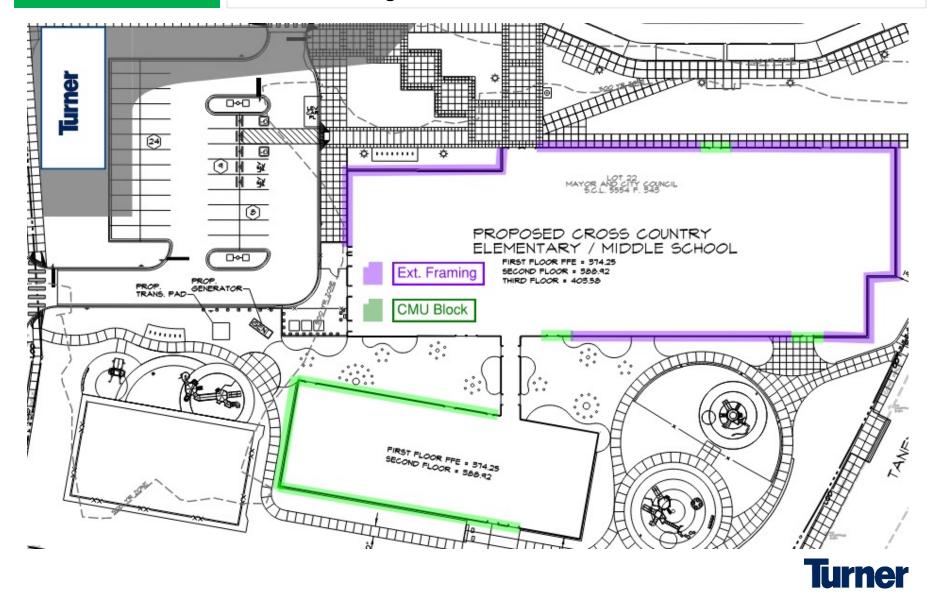


Exterior Framing







Exterior Sheathing

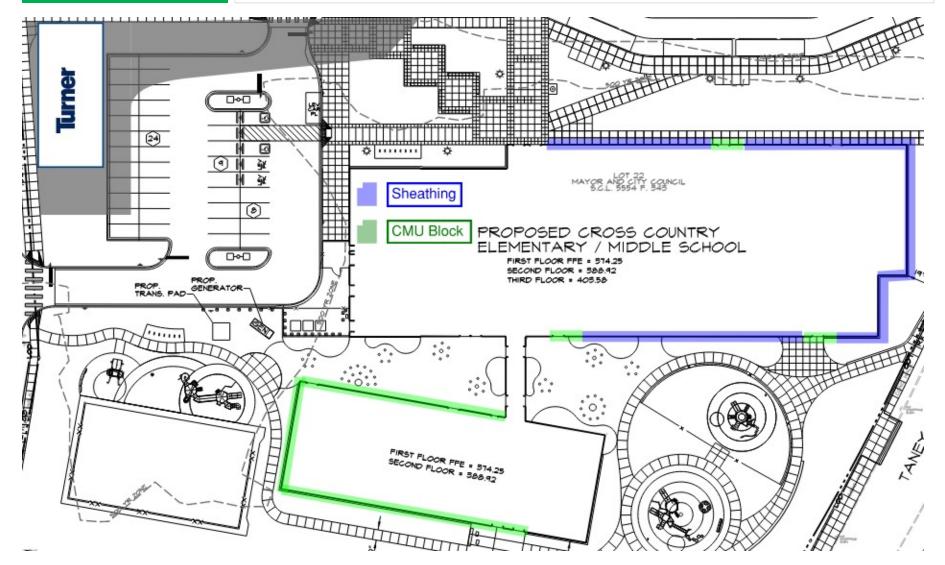




Exterior Sheathing







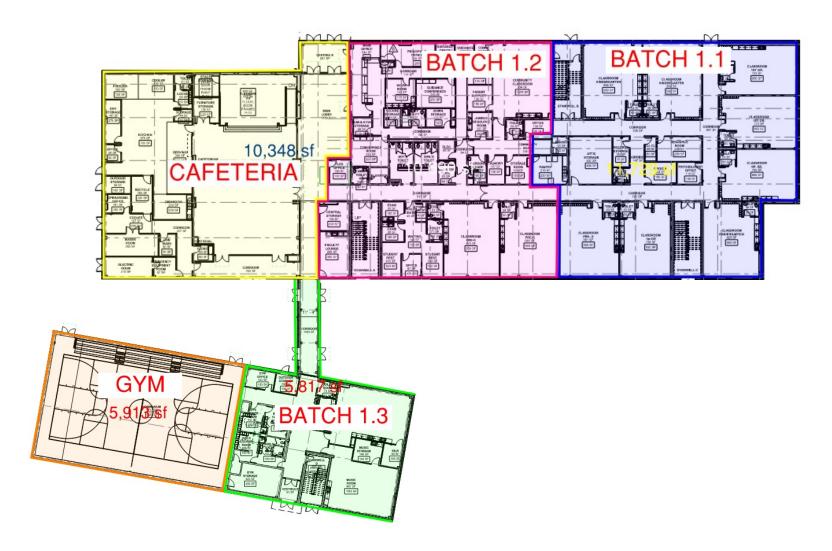



First Floor




Batch 1.1

Batch 1.2





Working Batches – Second Floor

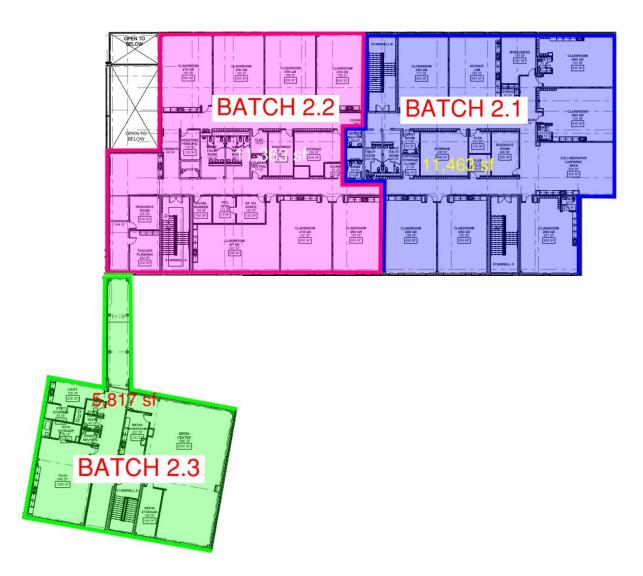



Second Floor




Batch 2.1

Batch 2.2



Site Utilities

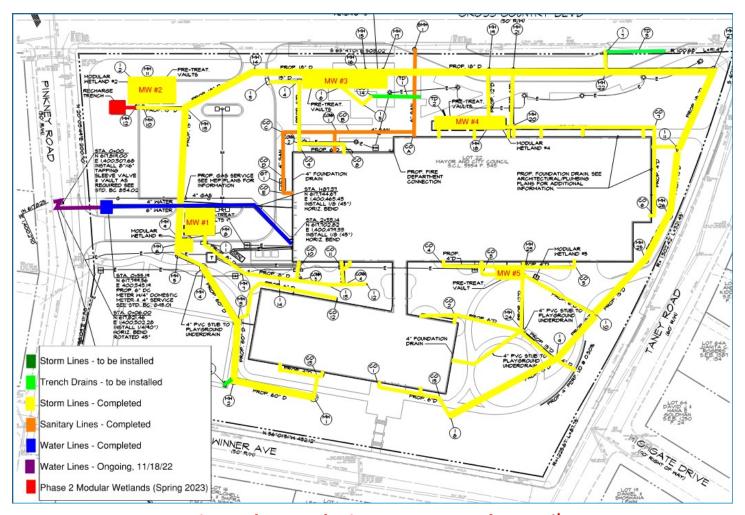

Projected Completion on November 18th
Phase 2 to Occur in Spring 2023




Project Site Parking Reminders

- If anyone parks in front of the hydrant on the corner of Pinkney & Winner, Turner
 will call to have it towed
- No one is to park within 10 feet of a corner
- All "No Stopping" signs are to be strictly followed
- Turner/MSA parking spots are to be followed
- All cars should be parked reasonably close to each other. No leaving ½ car length between cars
- All cars need to face the proper direction
- Turner has identified areas of No Parking, but does not have authority to enforce this request



Parking

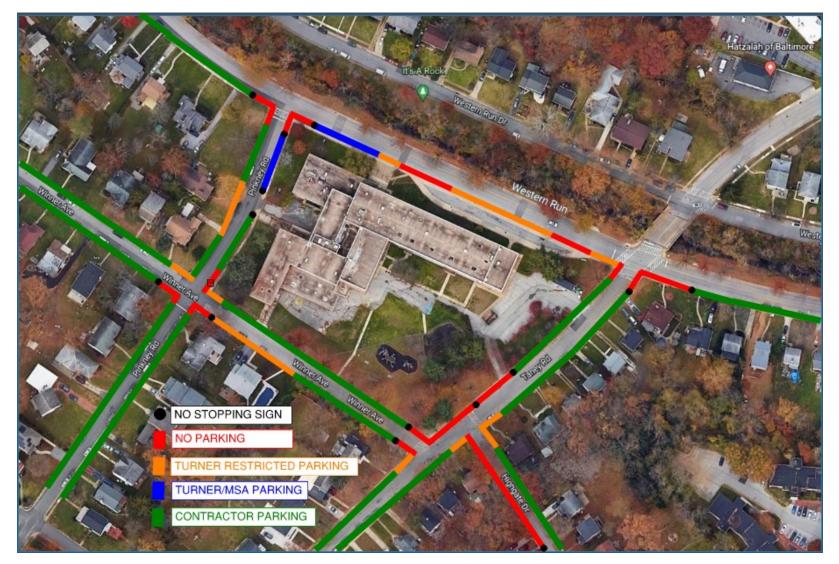




November 2022 – January 2023

Activity	Dates
Final Concrete Slabs	November 10 th Completion
Water Service Installation	November 18 th Completion
Exterior Framing & Sheathing	December 15 th Completion
Phase 1 Roofing	December 15 th Completion
Electrical Ductbank Installation	December 31 st Completion
Exterior Brick	December 1 st Start
Ceiling Rough-in 2 nd Floor	January 17 th Completion
Interior Wall Rough-in 1st Floor	January 31 st Completion



www.baltimore21stcenturyschools.org @21stCenturySchoolBuildingProgram









Questions?

Program Contacts

Sr. Community & Public Relations Coordinator Ivy McNeill

idmcneill01@bcps.k12.md.us

Community & Public Relations Manager Renee Stainrod

rastainrod@bcps.k12.md.us

Program Information

21st Century School Buildings Program Office (443) 642-4600



Thank You.

This presentation was brought to you by the 21st Century School Buildings Program.

By joining this presentation your email will be added to our program communications regarding this project.

www.baltimore21stcenturyschools.org

21st Century School Buildings Program

Baltimore City Public Schools 200 East North Avenue Room 407-B Baltimore MD 21202 (443) 642-4600

Cynthia Smith

Executive Director, Facilities Planning, Design & Construction Baltimore City Public Schools

Gary McGuigan

Executive Vice President, Capital Development Division Maryland Stadium Authority

Dr. Debra Y. Brooks

Executive Director Mayor's Office of Children and Family Success

Alex Donahue

Interim Executive Director, Public School Construction Program State of Maryland







