



21st Century School Buildings Program

GOVANS ELEMENTARY SCHOOL

CONSTRUCTION UPDATE COMMUNITY MEETING | November 24, 2020

BALTIMORE CITY
PUBLIC SCHOOLS



Introductions**Renee Stainrod**

Manager, Community & Public Relations
21st Century School Buildings Program

Alicia Thomas

Sr. Coordinator, Community & Public Relations
21st Century School Buildings Program

Tiara Moorman

Project Manager
Maryland Stadium Authority

Tim Schell

Project Architect
USA Architects

Amy Gorman

Project Manager
Dustin Construction

Agenda

- . **Introductions & Agenda**
- . **Site Logistics Plan**
- . **Project Schedule**
- . **Progress of Work to Date**
- . **Aerial Photos**
- . **Questions & Contact Info**

CONSTRUCTION

Site Logistics Plan – Steel Delivery through December 11, 2020


Delivery Times | Monday – Friday | 7 a.m. – 12 p.m.




Project Schedule – November/December

Steel Erection Completion

- Area C: 1st floor – complete
- Area C: 2nd floor – complete
- Area B: 1st floor – complete
- Area B: 2nd floor – complete
- Area B/C: 3rd floor – decking/detailing
- Area A: 1st floor – in progress

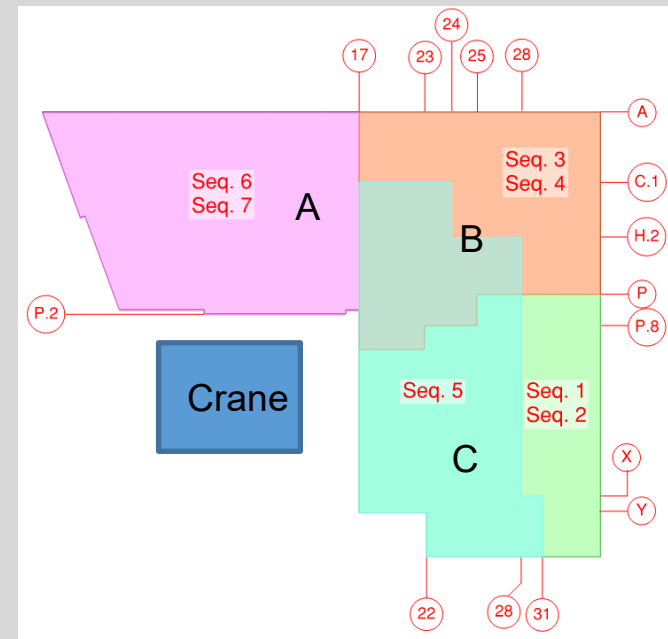

Project Schedule – November/December

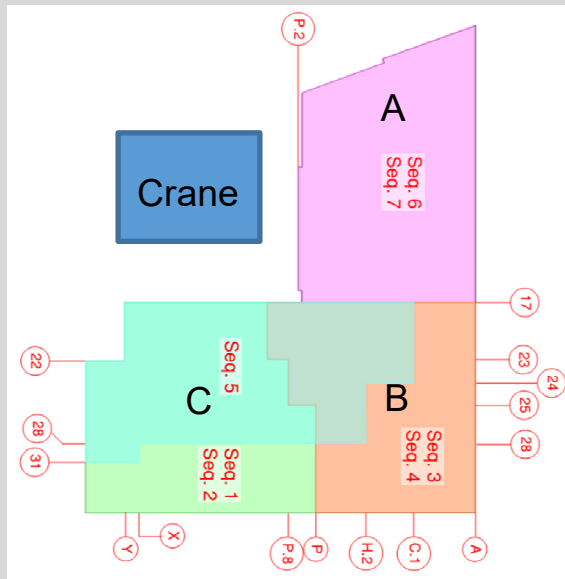








Slab on Deck

- Area C to B: 1st floor – complete
- Area C to B: 2nd floor – complete
- Area B to A: 1st floor – week of December 1
- Area A: 1st floor – week of December 8

Project Schedule – December/January

Roofing


- Roof E 
- Roof F 
- Roof G 
- Roof A 
- Roof C 
- Roof D/B 

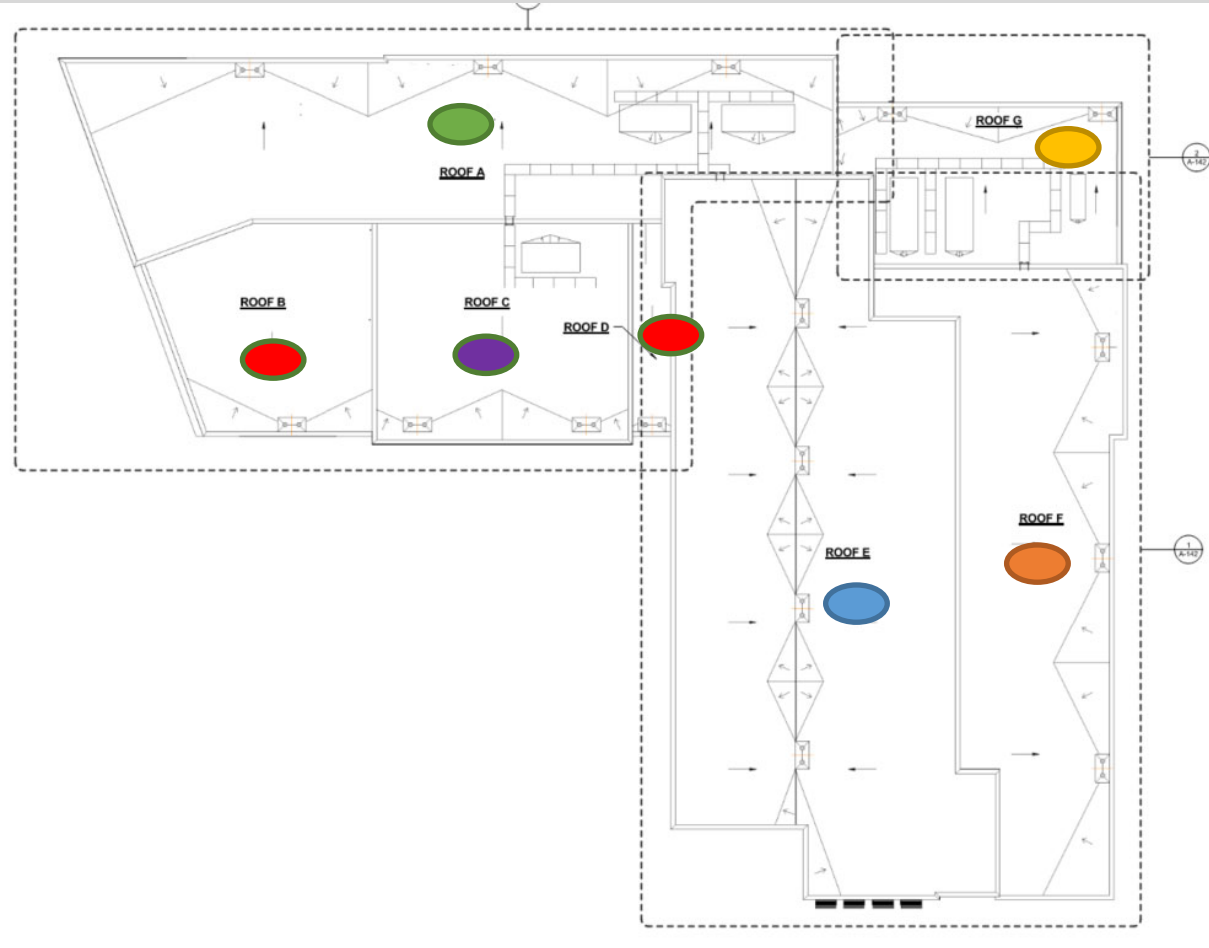

Project Schedule – December/January

Veneer

- Area C - South
- Area C/B - East
- Area C - West
- Area B/A - North
- Area A – West
- Area A - South

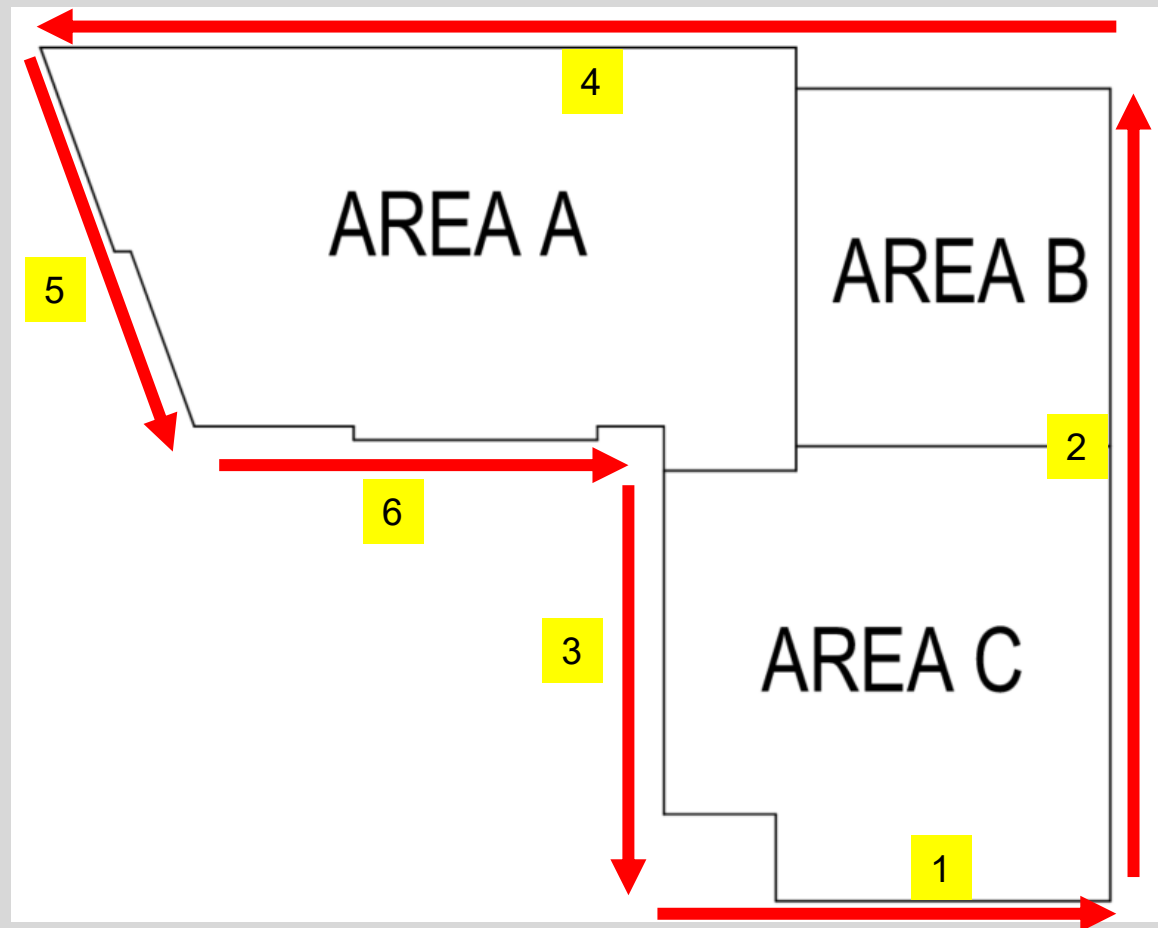


Progress

- Steel Erection



Progress

Slab on deck 1st and 2nd Floors – Area C/B

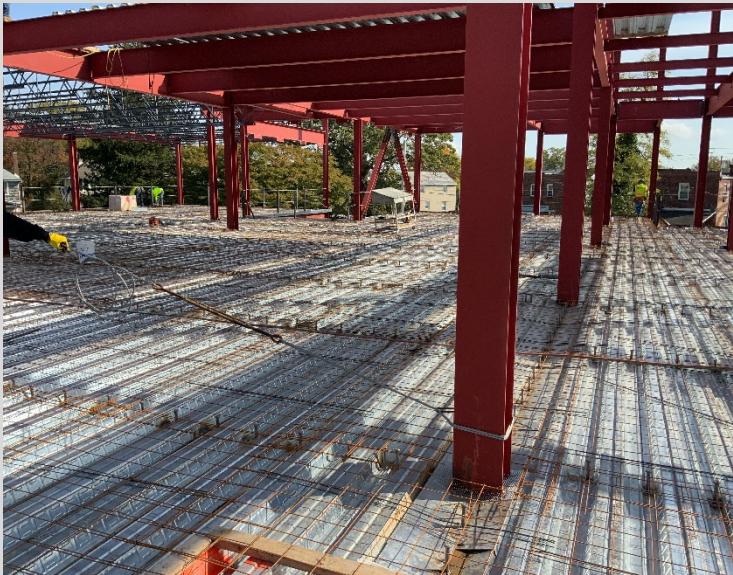

Progress

MEP's 1st Floor Area C
Interior Framing Area C



Progress

Group Bathrooms 1st Floor Area C – RI's
MEP's 1st Floor Area C



Progress



Interior Stair – Area A



Progress

CFMF at Exterior 1st Floor



Progress

Sheathing at Exterior 1st Floor – Area C



Progress

Retaining wall at Cording Avenue



CONSTRUCTION

Aerial Photo – July 2020



CONSTRUCTION

Aerial Photo – August 2020



CONSTRUCTION

Aerial Photo – September 2020



CONSTRUCTION

Aerial Photo – October 2020



CONSTRUCTION

Aerial Photo – November 2020



Thank You!



This presentation is brought to you by the
21st Century School Buildings Program.

www.baltimore21stcenturyschools.org

21st Century School Buildings Program

Baltimore City Public Schools
200 East North Avenue Room 407-B
Baltimore MD 21202
(443) 642-4600

Dorothy Hellman

Executive Director, 21st Century School Buildings Program
Baltimore City Public Schools

Gary McGuigan

Senior Vice President, Capital Development Division
Maryland Stadium Authority

Tisha Edwards

Mayor's Health, Human Services, Education and Youth
City of Baltimore – Office of Children and Family Success

Robert Gorrell

Executive Director, Public School Construction Program
State of Maryland

BALTIMORE CITY
PUBLIC SCHOOLS



Questions?

Program Information

21st Century School Buildings Program Office
(443) 642-4600

Sr. Community & Public Relations Coordinator
Alicia Thomas
athomas03@bcps.k12.md.us

Community & Public Relations Manager
Renee Stainrod
rastainrod@bcps.k12.md.us

Construction Manager Project Manager
Amy Gorman
agorman@dustinconstruction.com
(301)252-7714



21stCenturySchoolBuildingsProgram



21stCSBaltimore



21stCSBaltimore

www.baltimore21stcenturyschools.org
