

## 21st Century School Buildings Program

GOVANS ELEMENTARY SCHOOL
CONSTRUCTION UPDATE COMMUNITY MEETING | April 28, 2021







#### Introductions & Agenda

#### Introductions

#### **Renee Stainrod**

Manager, Community & Public Relations 21st Century School Buildings Program

#### **Alicia Thomas**

Sr. Coordinator, Community & Public Relations 21st Century School Buildings Program

#### **Tiara Moorman**

Project Manager Maryland Stadium Authority

#### **Tim Schell**

Project Architect
USA Architects

#### **Amy Gorman**

Project Manager
Dustin Construction

#### Agenda

- Introductions & Agenda
- Project Schedule
- Progress of Work to Date
- **Aerial Photos**
- **Community Meeting Info**
- Questions & Contact Info


## Project Schedule – December/January

#### Masonry Veneer

- Area C East & South complete
- Area C West complete
- Area B East complete
- Area A North complete
- Area A West complete
- Area A South complete

#### Windows – Start Date 2/15/2021

- Area C East/South complete
- Area C West complete
- Area B complete
- Area A complete
- Area A complete

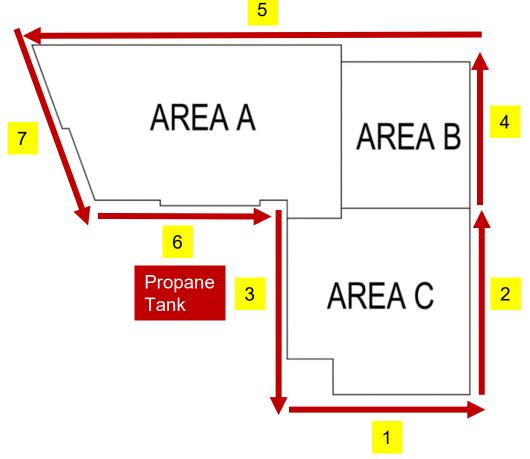

## **Progress**







## Project Schedule – January/February


### Roofing

- → Roof E complete
- → Roof F complete
- → Roof G complete
- → Roof A complete
- $\bigcirc$   $\rightarrow$  Roof C complete
- → Roof D/B complete

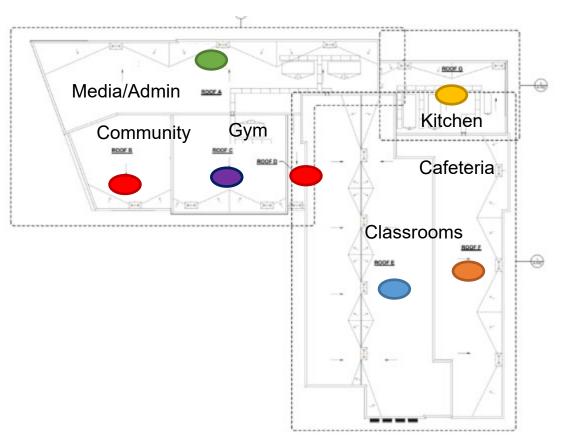


## **Progress**

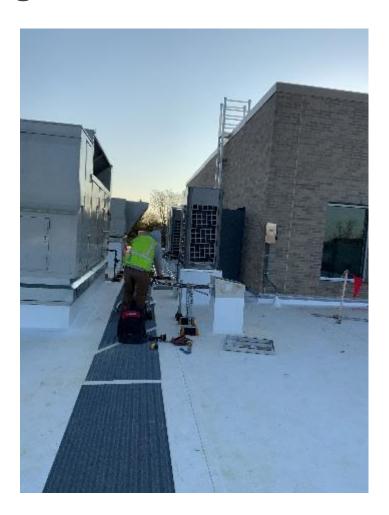

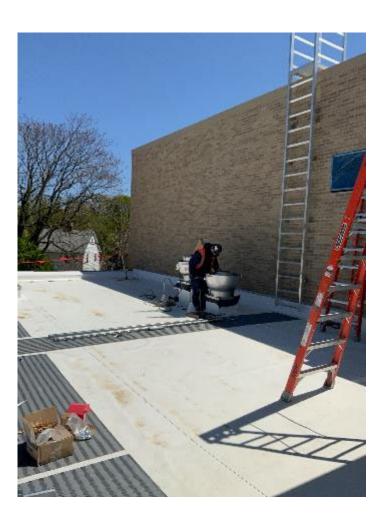

# Project Schedule – February/March

- Electrical/Telecom Room
- All Areas/Floors

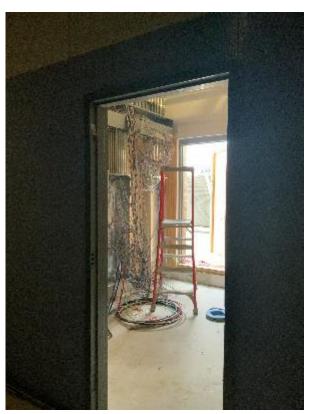





## Progress-February/March/April

### Hanging/Tape/Finishing

- Area  $C 1^{st} 3^{rd}$  complete
- Area  $B 1^{st} 2^{nd}$  complete
- Area A 1<sup>st</sup> 2<sup>nd</sup> complete





## Progress-March/April







# Project Schedule – March/April/May

Item	Time	Status
Ceramic Tile	April	Completed
Light Fixtures	April	In Progress
VCT Flooring	May	
Epoxy Flooring	May	
Casework	May	
Marker/Tack boards	May	





# Progress-April/May/June







### Aerial Photo – July 2020



### Aerial Photo – August 2020



### Aerial Photo – September 2020



#### Aerial Photo – October 2020



#### Aerial Photo – November 2020



#### Aerial Photo – December 2020




### Aerial Photo – January 2021



## CONSTRUCTION

### Aerial Photo – February 2021

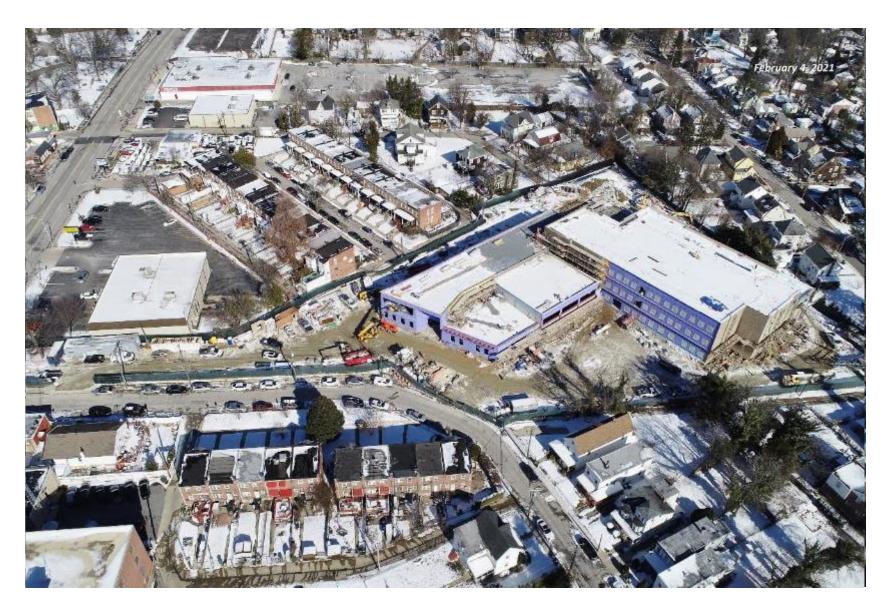

#### Aerial Photo – March 2021



### Aerial Photo – April 2021



### **Community Meeting Info**

#### www.baltimore21stcenturyschools.org @21stCenturySchoolBuildingProgram









## **Questions?**

## **Project Contacts**

Sr. Community & Public Relations Coordinator

Alicia Thomas athomas 03@bcps.k12.md.us

**Community & Public Relations Manager** 

Renee Stainrod rastainrod@bcps.k12.md.us

#### **Construction Manager Project Manager**

Amy Gorman agorman@dustinconstruction.com (301)252-7714

## **Program Information/Contacts**

**21**st Century School Buildings Program Office (443) 642-4600







21stCSBaltimore

21stCenturySchoolBuildingsProgram

21stCSBaltimor

#### Thank You!



This presentation is brought to you by the 21st Century School Buildings Program.

### www.baltimore21stcenturyschools.org

#### 21st Century School Buildings Program

Baltimore City Public Schools 200 East North Avenue Room 407-B Baltimore MD 21202 (443) 642-4600

#### **Dorothy Hellman**

Executive Director, 21<sup>st</sup> Century School Buildings Program Baltimore City Public Schools

#### **Gary McGuigan**

Senior Vice President, Capital Projects Development Group Maryland Stadium Authority

#### **Tisha Edwards**

Director, Mayor's Office of Children & Family Success City of Baltimore

#### **Robert Gorrell**

Executive Director, Public School Construction Program State of Maryland







