



21st Century School Buildings Program

GOVANS ELEMENTARY SCHOOL

CONSTRUCTION UPDATE COMMUNITY MEETING | June 23, 2021

BALTIMORE CITY
PUBLIC SCHOOLS



Introductions**Renee Stainrod**

Manager, Community & Public Relations
21st Century School Buildings Program

Alicia Thomas

Sr. Coordinator, Community & Public Relations
21st Century School Buildings Program

Tiara Moorman

Project Manager
Maryland Stadium Authority

Tim Schell

Project Architect
USA Architects

Amy Gorman

Project Manager
Dustin Construction

Agenda

- . **Introductions & Agenda**
- . **Project Schedule**
- . **Progress of Work to Date**
- . **Aerial Photos**
- . **Community Meeting Info**
- . **Questions & Contact Info**

CONSTRUCTION

Construction Phase – Completed & In Progress Items

December/January

- Masonry Veneer

January/February

- Roofing Membrane

February/March

- Windows
- Electrical Room Buildouts

March/April


- Hanging/Taping/Finishing

April/May

- Interior Painting/Dropping Ceiling Tile

May/June

- Site Work

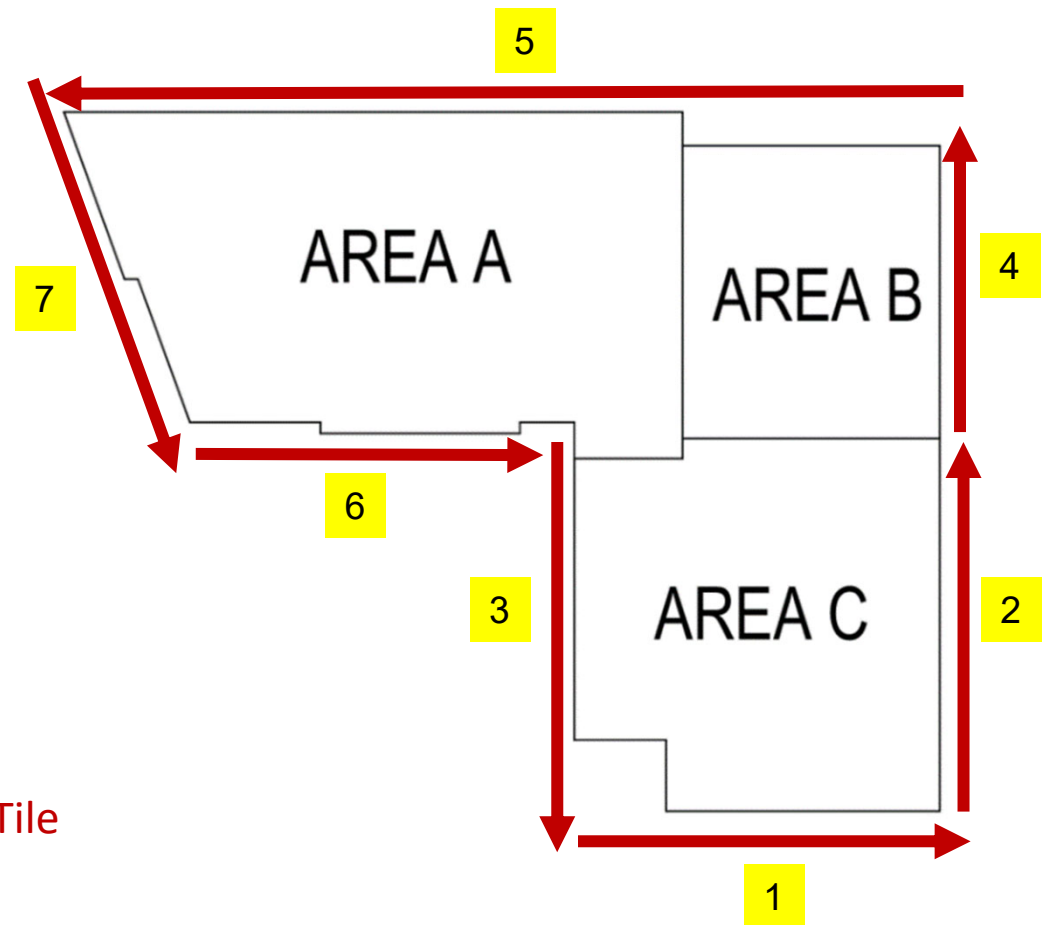


Project Schedule – April/May/June/July

Item	Time	Status
Ceramic Tile	April	Completed
Light Fixtures	April/May/June	In Progress
VCT Flooring	May/June	In Progress
Epoxy Flooring	May/June	Completed
Casework	May/June	In Progress
Marker/Tack boards	May/June	In Progress
Metal Panels	June	In Progress
Specialty Ceilings	June	In Progress



Progress

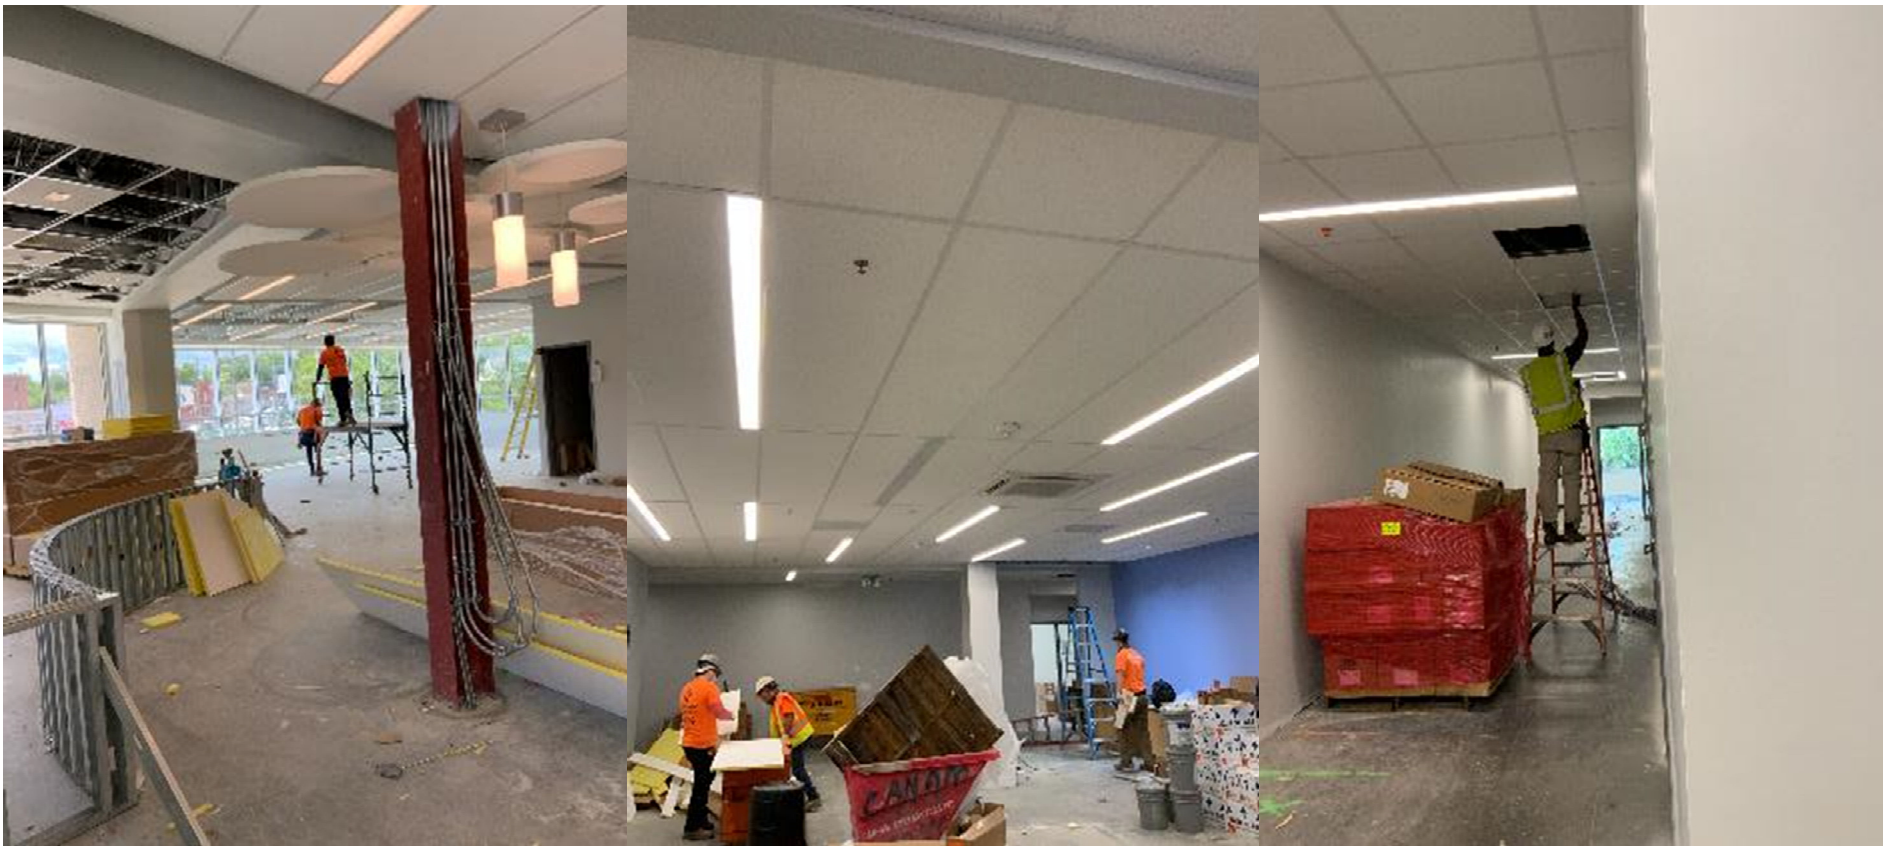

CONSTRUCTION

Construction Phase – Epoxy Flooring at bathrooms & kitchen

Progress



Progress



Progress



Progress



Progress



Progress




Progress



Project Schedule – COMING SOON!

Playground Equipment
Gym Equipment
Media Center - Carpet
Stage/Dining – Wood Floors
Parking Lot
Landscaping

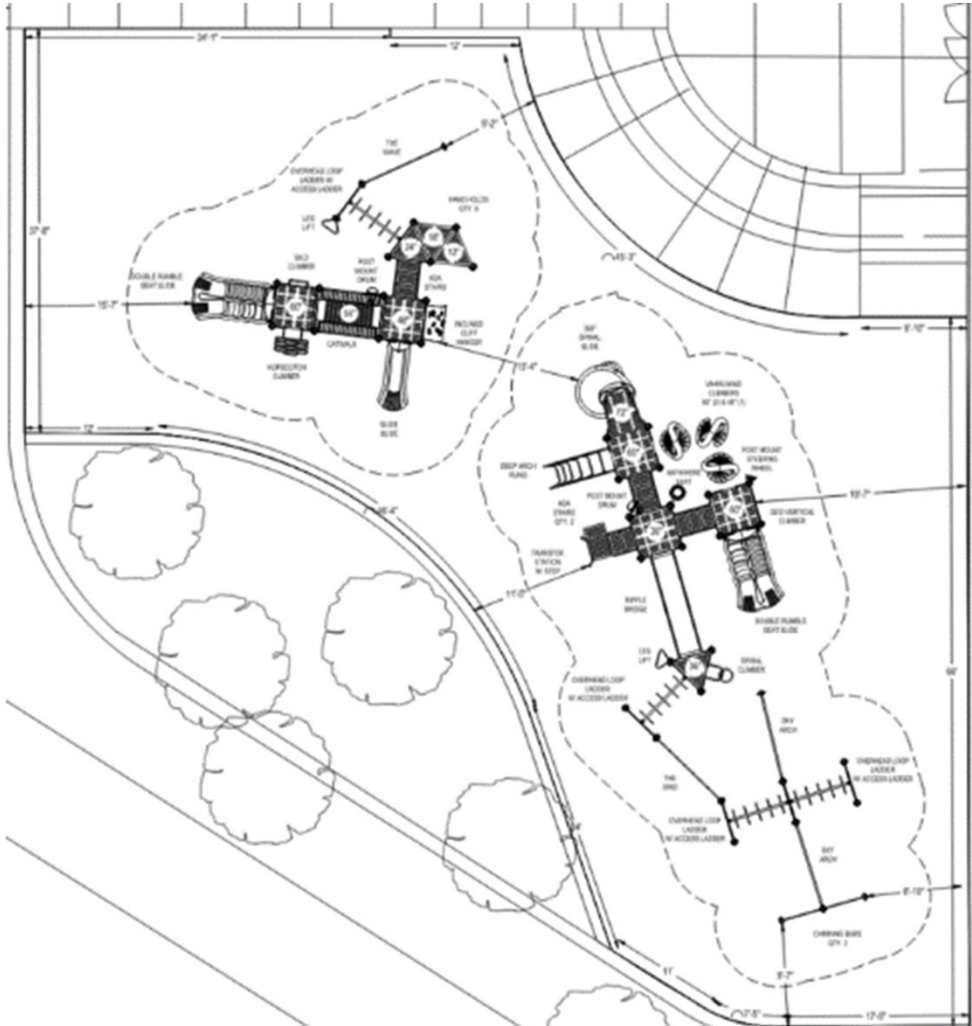

CONSTRUCTION

Construction Phase – Playground Equipment



Govans Elementary School

playground
Specialists Inc.



CONSTRUCTION

Aerial Photo – July 2020



CONSTRUCTION

Aerial Photo – August 2020



CONSTRUCTION

Aerial Photo – September 2020



CONSTRUCTION

Aerial Photo – October 2020



CONSTRUCTION

Aerial Photo – November 2020



CONSTRUCTION

Aerial Photo – December 2020



CONSTRUCTION

Aerial Photo – January 2021



CONSTRUCTION

Aerial Photo – February 2021



CONSTRUCTION

Aerial Photo – March 2021



CONSTRUCTION

Aerial Photo – April 2021



CONSTRUCTION

Aerial Photo – May 2021





CONSTRUCTION

Aerial Photo – June 2021



www.baltimore21stcenturyschools.org @21stCenturySchoolBuildingProgram



Questions?

Project Contacts

Sr. Community & Public Relations Coordinator

Alicia Thomas

athomas03@bcps.k12.md.us

Community & Public Relations Manager

Renee Stainrod

rastainrod@bcps.k12.md.us

Construction Manager Project Manager

Amy Gorman

agorman@dustinconstruction.com

(301)252-7714

Program Information/Contacts

21st Century School Buildings Program Office

(443) 642-4600



21stCSBaltimore



21stCenturySchoolBuildingsProgram



21stCSBaltimore

Thank You!



This presentation is brought to you by the
21st Century School Buildings Program.

www.baltimore21stcenturyschools.org

21st Century School Buildings Program

Baltimore City Public Schools
200 East North Avenue Room 407-B
Baltimore MD 21202
(443) 642-4600

Dorothy Hellman

Executive Director, 21st Century School Buildings Program
Baltimore City Public Schools

Gary McGuigan

Senior Vice President, Capital Projects Development Group
Maryland Stadium Authority

Tisha Edwards

Director, Mayor's Office of Children & Family Success
City of Baltimore

Robert Gorrell

Executive Director, Public School Construction Program
State of Maryland

BALTIMORE CITY
PUBLIC SCHOOLS

